

TREE PROTECTION PLAN

METHOD OF TREE PROTECTION

Measures for Tree Protection during Construction Works.
Tree Protection Plan (TPP) to identify:

- Trees to be retained and trees to be removed.
- Protective fence positions therefore the Construction Exclusion Zone (CEZ).
- Measurements to identify fence positions.
- Area available for working and storage space.

1. **Order of works**



- Observe general precautions note.
- Carry out prescribed tree removals and hedge trimming.
- Erect protective fencing as shown on this Tree Protection Plan.
- Construct new development.
- Only when the work is complete can the protective fencing be removed.

General precautions

- 2. If bonfires are lit on site these must be kept 15m away from any tree. Nothing is to be attached to any tree.
- 3. **The construction exclusion zones** are afforded protection at all times. No works will be done within any CEZ. There will be no access required to the CEZ for construction work.
- 4. The grade level must not be changed within the CEZ without approval of the project arboriculturist.
- 5. **A protective fence** shall be erected prior to commencement of any site works. The fence shall have signs attached to it stating that it is a Construction Exclusion Zone and that NO WORKS are PERMITTED within the fence. The fence may only be removed following completion of all the works.

- 6. The fence is required to be sited in accordance with this Tree Protection Plan. It must be constructed as shown and be fit for the purpose of excluding construction activity. Any other type of barrier used must be fit for the purpose and agreed by the project arboriculturist.
- 7. **Storage space** can be allocated away from CEZs and provisions must be made to ensure that CEZs cannot become contaminated by stored materials, chemical leaching, or run off from storage areas.
- 8. **The general use of herbicide** is not planned on the site. Herbicides must not be used for this project, without the advice of the project arboriculturist.

- NOTES:
1. This drawing and the information it contains, may not be used or copied, without the express written permission of Wayne Isaacson Tree Consultancy Ltd ©2025.
 2. This plan must be distributed to the site manager, and a copy displayed on the site notice board.
 3. This drawing was produced in colour, a monochrome copy should not be relied upon.
 4. Ordnance Survey Licence number 100053138.

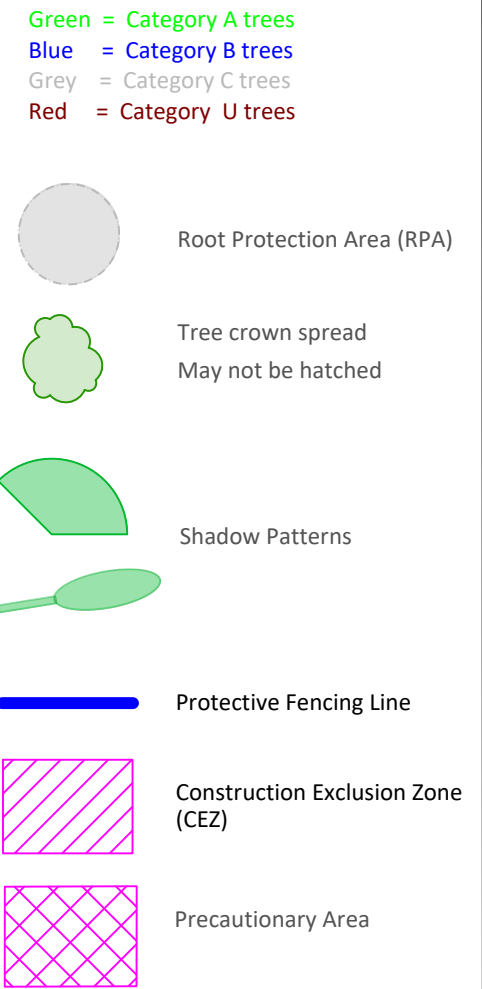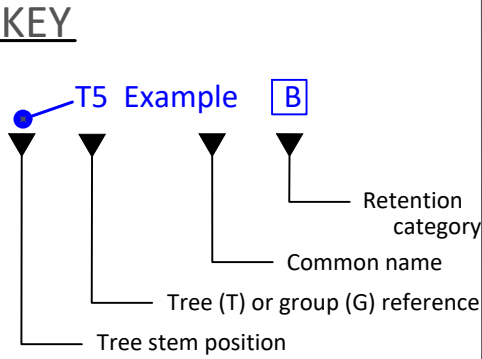

WAYNE ISAACSON
TREE CONSULTANCY LTD
www.wayneisaacson.co.uk
wayne@wayneisaacson.co.uk
07714460269

Reference WIT-25-14-005-TPP-A

Scale 1:200 @ A2
Client Mr Fairclough

Drawn by WI
Date 03/09/2025

Site Land adjacent to 3 Brickfield Cottages, East Cowes Road, Isle of Wight, PO32 6NH

Title Tree Protection Plan

